



SAN BRUNO RECREATION & AQUATIC CENTER

Advisory Committee Update

January 19, 2022



AGENDA

1. Construction Update and Look Ahead Schedule

- a) Project Information Update
- b) Completed To Date
- c) Schedule Update
- d) Change Orders Report
- e) What's Happening Next 30 Days

2. Questions

Construction Update and Look Ahead Schedule



PROJECT INFORMATION



Start Date: September 2021




Project Completion: Fall 2023



Estimated Cost Completed To Date: 5%(December 2021)



EarthCam Link: https://share.earthcam.net/RecCenterBuild/rec_center_build/camera/view_1

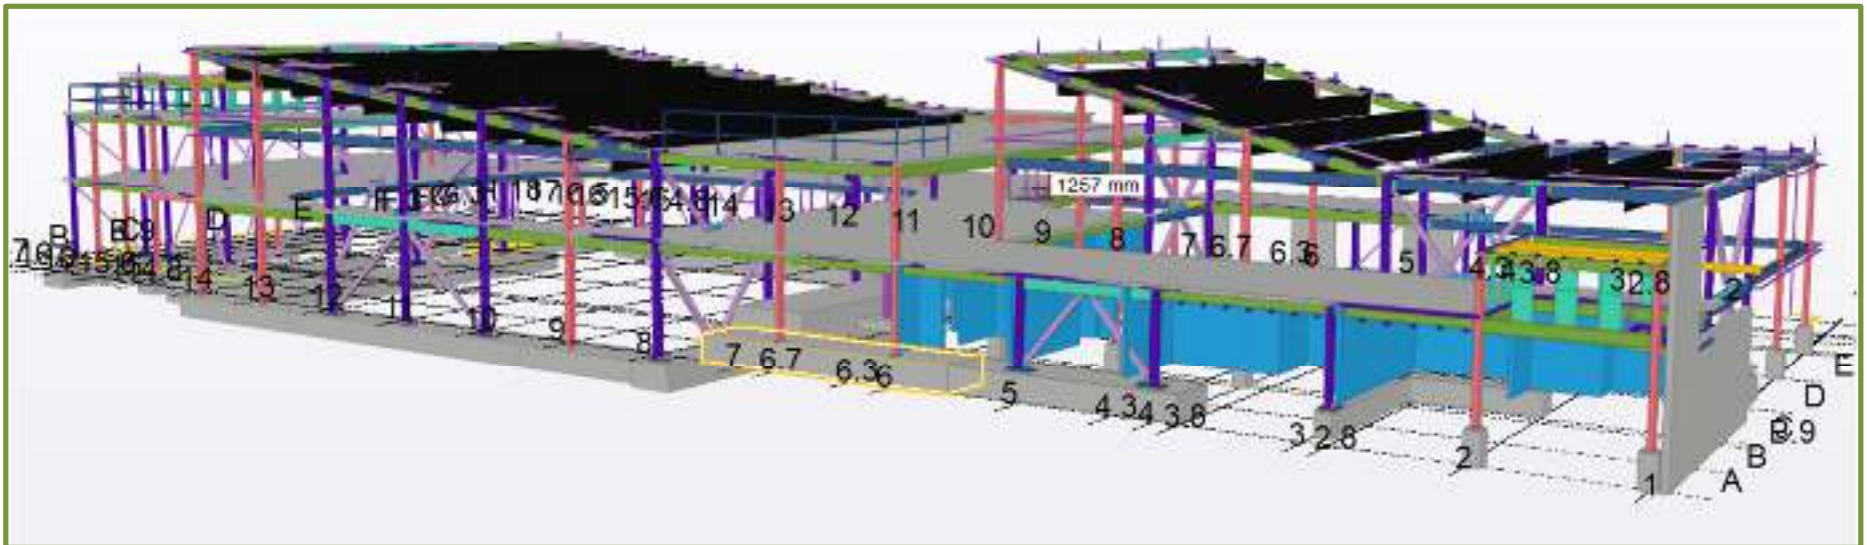

Construction Update and Look Ahead Schedule



☑ **COMPLETED TO DATE** (Through 01/14/22)

- Tree Removal (Crystal Springs Avenue)
- Temporary Water Line Bypass
- Retaining Wall Work - Mobilizing



TREE REMOVAL



TEMPORARY WATER LINE BYPASS



TEMPORARY WATER LINE BYPASS

Construction Update and Look Ahead Schedule




COMPLETED TO DATE *(Through 01/14/22)*

- Team Completed the review of 148 of the 177 submittals (Materials and Installation) and Resolved 119 of 137 RFI (Trades and Design Coordination)
- Geopier Structural Evaluation - Required Less Geopier (Resulted to contract savings)
- Building Frames – 800,000 lbs of Structural Steel - Fabrication



GEOPIER

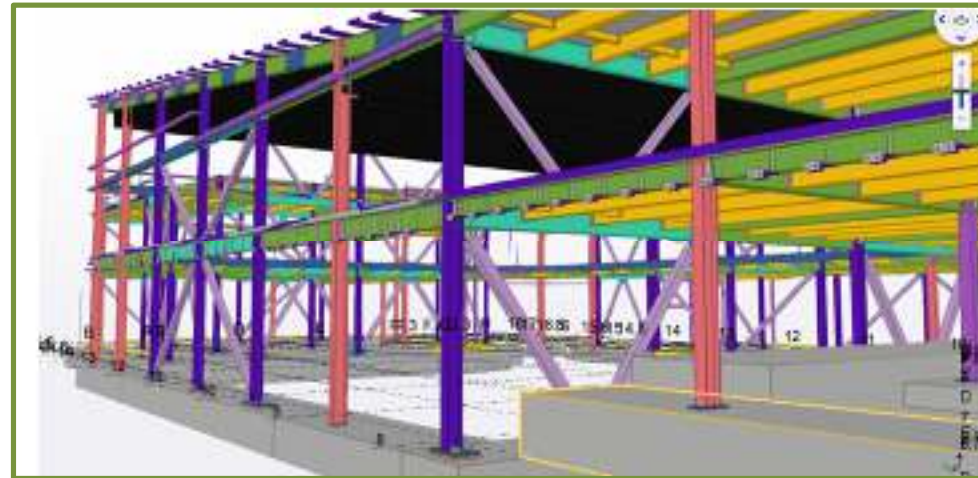


**STRUCTURAL
STEEL**

Construction Update and Look Ahead Schedule




SCHEDULE UPDATE

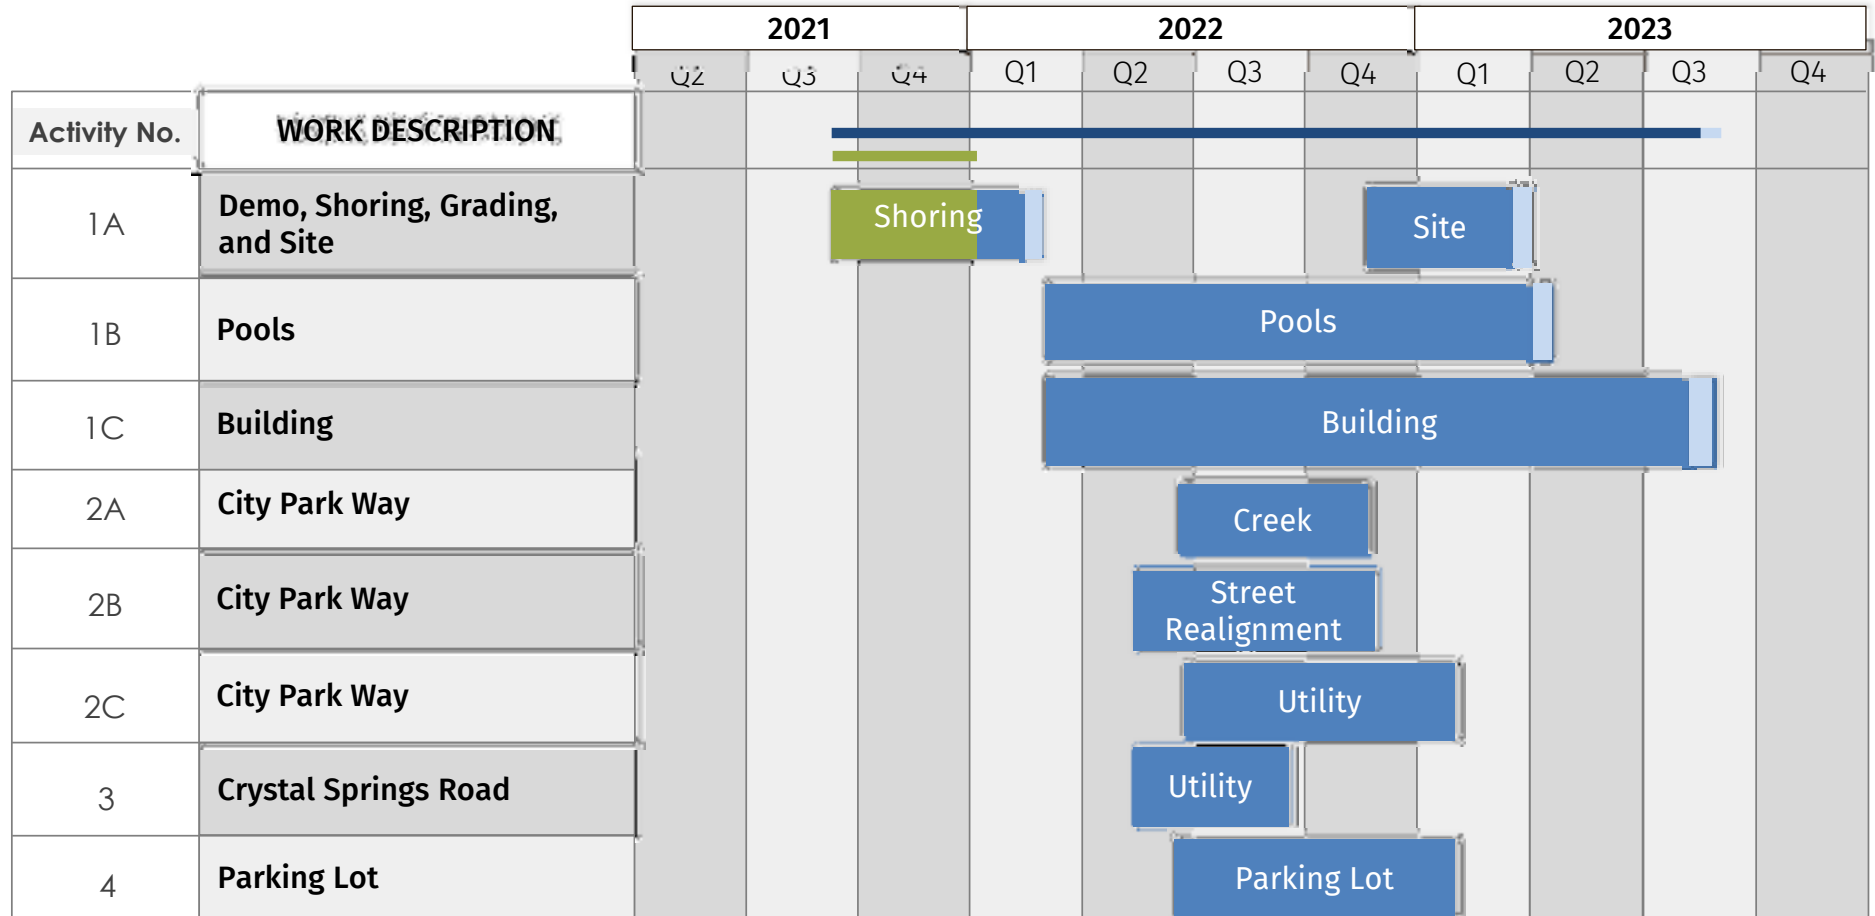

Construction Update and Look Ahead Schedule



Change Order Report – NO CHANGE

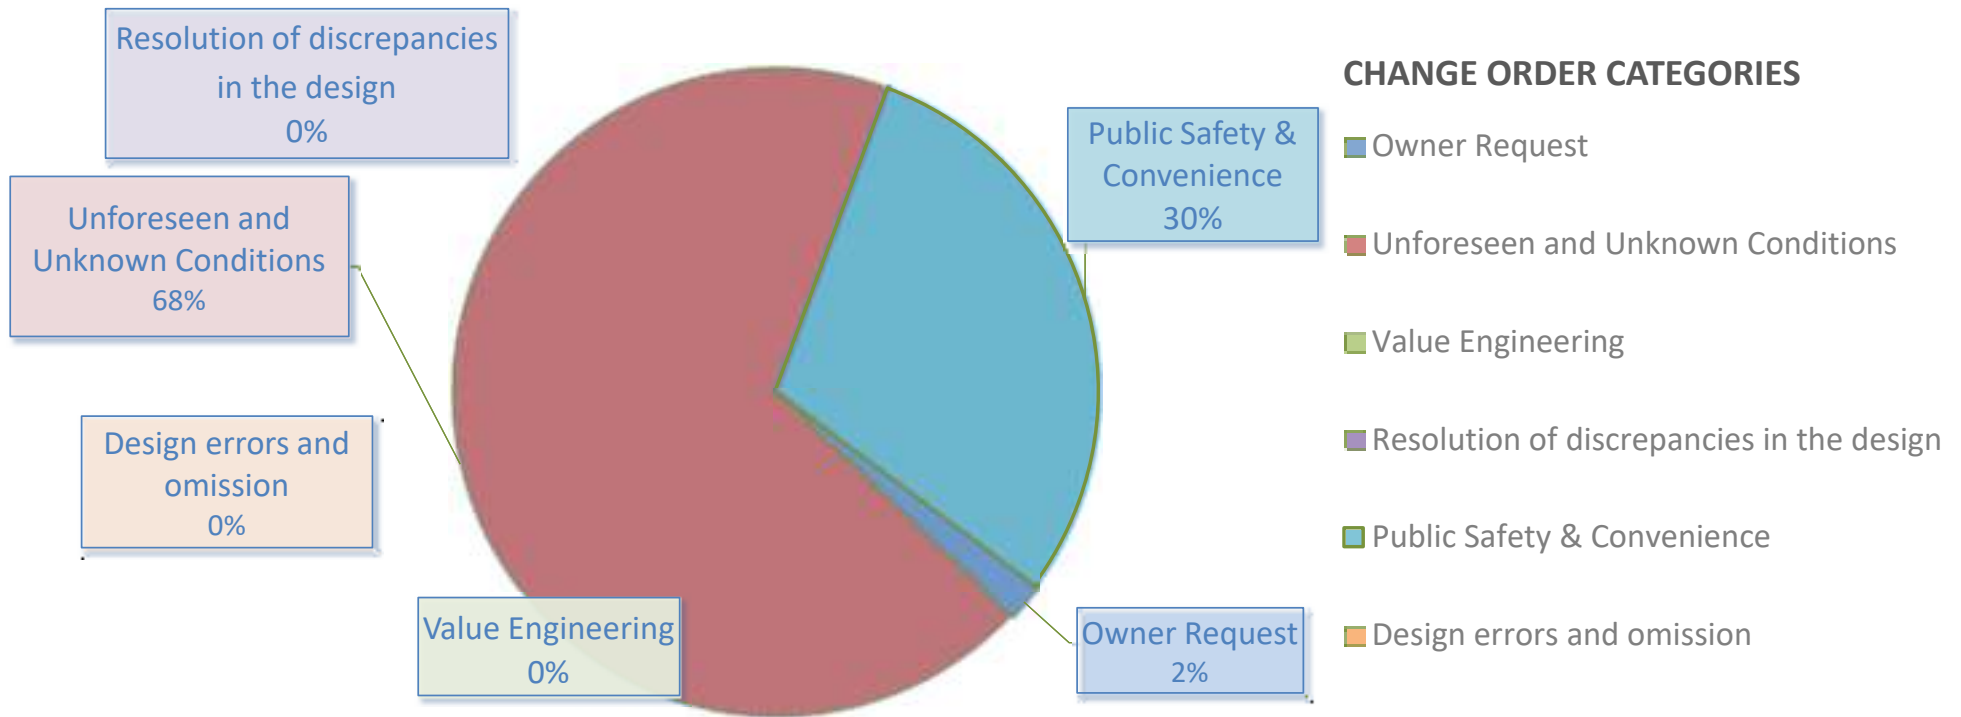

In-Process and Upcoming Under Review Change Orders

Construction Update and Look Ahead Schedule



WHAT'S HAPPENING NEXT 30 DAYS?


- Completing the Installation of temporary by-pass water line
- Removal of the Existing Water Line
- Grading and Retaining Wall (shoring)



REMOVAL OF EXISTING WATER LINE



RETAINING WALL

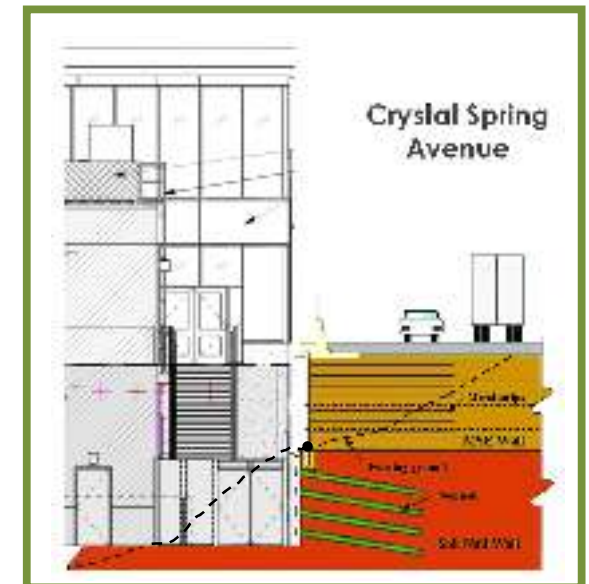

RETAINING WALL

THANK YOU

sanbruno.ca.gov/RecCenterBuild
