

# **Crestmoor Neighborhood Reconstruction**

Project Status Update
City of San Bruno City Council
October 22, 2019

Harry Burrowes, Project Manager – Crestmoor Reconstruction Project Keith DeMartini – Finance Director

# **Agenda**

Three Items Before City Council Tonight Related to the Crestmoor Reconstruction Project:


- Overall Project Summary and Funds Appropriation Request
- 2) Earl Glenview Park Closeout
  - Request to Amend Contractor and Project Designer Agreements
  - Acceptance of Project as Complete
- 3) Phase IV Street Improvement Project Partial Release of Retention to Contractor

# Overall Project Summary

- Overview of PG&E Trust
  - Components & Expenditures
- Reconstruction Projects
  - Completed Projects
  - Current Project
- Remaining Items to Complete
- Contract amendments required for closeout
- Strategy to cover the budget shortfall

# **PG&E Trust Fund Expenditures**

ltem	Percent of Total Cost
<u>item</u>	Cost
Reconstruction & Maintenance Costs	68.4 %
Regular and Contract Staff Time	15.3 %
Professional Services – Federal & State Proceedings	12.8 %
Administrative and Other Costs	3.5 %
TOTAL	100 %

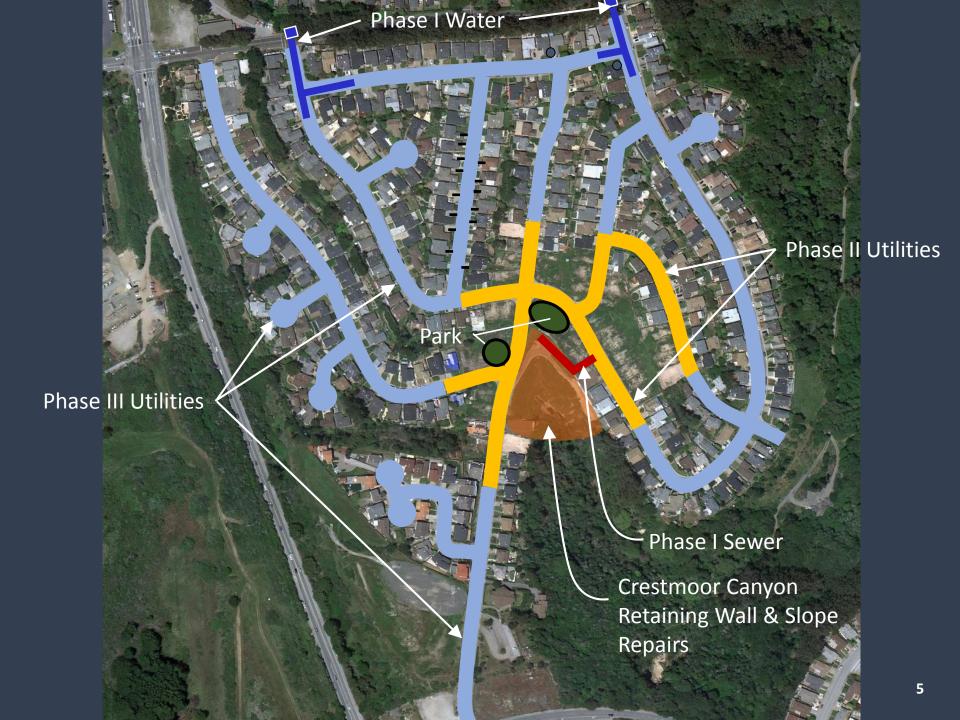

# **Completed Projects**

- Crestmoor Canyon Retaining Wall & Slope Repairs
- Phase I Sewer Main Replacement
- Phase I Water System Improvements
- Phase II Underground Utility Replacement
- Phase III Underground Utility Replacement
- ☐ Upper Sanitary Sewer Lateral Replacement Project
- ☐ Earl Glenview Park
- Crestmoor Canyon Replanting

# Remaining Project

Phase IV Street Improvements



# Crestmoor Canyon Slope & Retaining Wall Reconstruction





# Phase I Water & Sewer Reconstruction











# Phases II & III Utility Replacement

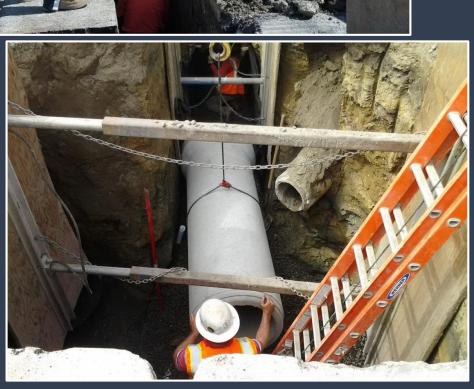




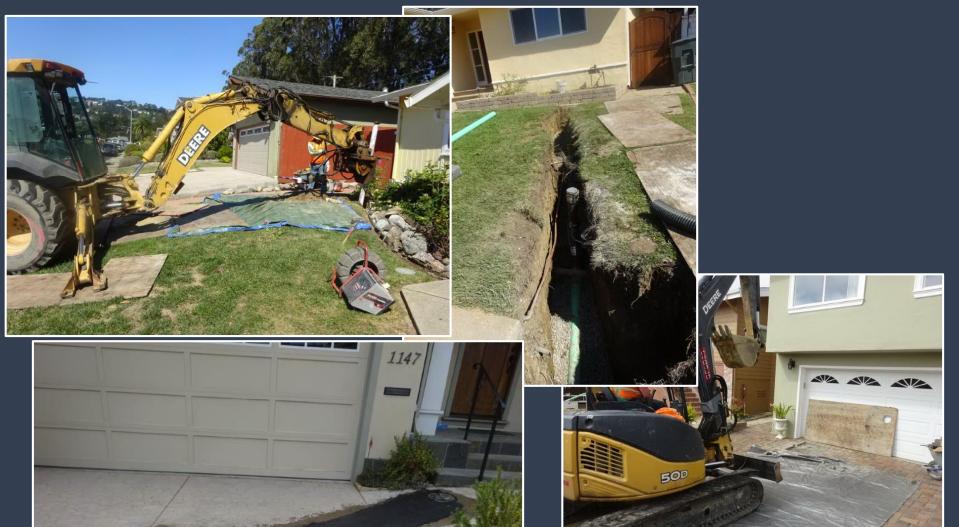

<u>Upper Sanitary Sewer</u> <u>Lateral Replacement</u>



# **Earl-Glenview Park**

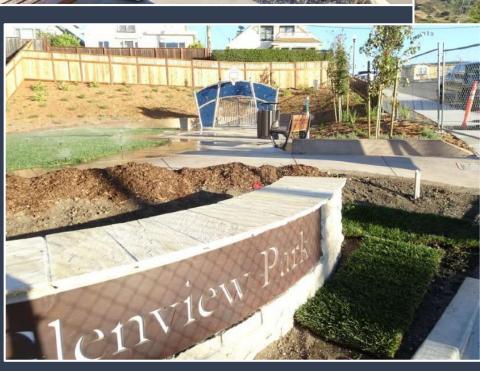



# Crestmoor Canyon Upper Slope Planting



# **Phase IV Street Improvements Project**







# **Earl-Glenview Park Closeout**

#### **Earl-Glenview Park Closeout**

- Ribbon cutting and opening of park in late October 2018
- Additional work completed summer 2019
- Contract amendments required for contractor (Elite Landscape) and designer (MIG, Inc.)
- Project deemed complete and ready for closeout





#### Earl-Glenview Park Closeout cont'd

Construction - Elite Landscape

Total Construction Budget \$ 1,204,683

Amount over Construction Budget \$ 26,090 (2.2%)

Design – MIG, Inc.

Total contract \$ 118,250

Amount over design budget \$ 6,400 (5.4%)





# **Phase IV Project and Closeout**

#### Reconstruction Project Items to Complete

- Phase IV Street Improvements
  - Final "punch-list" items
  - Pavement repairs
  - Concrete walkway adjustments
  - Intersection striping changes
  - Final clean-up (yard/signage)
- Project Record Drawings ("As-builts")
- Record of Survey
- Final Project Archiving

#### **Phase IV Street Improvements**

Partial Release of Retention to Contractor (Graniterock Construction Co., Inc.)

Total construction budget	\$ :	10,750,000
Total contract to date	\$ :	10,218,756
Total retention to date	\$	513,353
Remaining "liability" incl.	~ \$	50,000
contract and punch list		

Recommendation to release portion of remaining retention (\$250,000)

OVERALL CRESTMOOR RECONSTRUCTION COST			
<u>Item</u>	Expenditures to Date (thru June 2019)	Estimated Costs to Complete	<u>Total Cost</u>
Regular and Contract Staff Time	\$ 7,720,551	\$ 0	\$ 7,720,551
Community Support & Outreach	\$ 216,835	\$ 0	\$ 216,835
Professional Services – Federal & State Proceedings	\$ 6,451,040	\$ 0	\$ 6,451,040
Reconstruction & Maintenance Costs	\$ 33,494,433	\$ 1,096,500	\$ 34,590,933
Waived Fees	\$ 816,231	\$ 0	\$ 816,231
PG&E Trust & Trustee Costs	\$ 379,178	\$ 60,000	\$ 439,178
San Bruno Community Foundation	\$ 55,253	\$ 0	\$ 55,253
Asset Transfer Loss	\$ 299,864	\$ 0	\$ 299,864
TOTALS	\$ 49,433,386	\$1,156,500	\$50,589,886

Total Projected Budget Shortfall \$590,000

#### Keith DeMartini – Finance Director

# Strategy to Cover the Budget Shortfall & Fund Appropriation Request

# **Budget Summary**

Total Budget \$50,000,000

Total Projected Costs 50,590,000 est.

Projected Budget Shortfall (\$ 590,000)

# **Budget Balancing Solutions**

Fund 004 (Fire Station 52) 100,000

Fund 190 (Staff Costs on Reserve) 490,000

Projected Budget Shortfall \$0

# **Strategies to Cover Budget Shortfall**

- Capital Improvement/One-Time Initiative Reserve Fund (Fund 004)
  - \$100,000 of staff and consultant costs related to Fire Station 52
- Emergency Disaster Recovery Fund (Fund 190)
  - \$722,000 of staff costs paid by the trust that was put on reserve
  - Request to use \$490,000 to cover the budget shortfall
  - Upon project close-out, a final fund reconciliation will be conducted to address any remaining costs and close the fund and capital project.

# Request to City Council (1 of 3)

Receive Presentation and Update on the Crestmoor (Glenview Fire) Neighborhood Reconstruction Project and Adopt Resolution:

- Authorizing Appropriation of \$100,000 from the Capital Improvement/One-Time Initiative Reserve Fund (Fund 004) to Cover the Costs Associated with Fire Station 52 Geotechnical Work; and,
- Authorizing \$490,000 of Staff Time on Reserve in the Emergency Disaster Recovery Fund (Fund 190) for the Remaining Expenditures in Order to Complete the Project

# Request to City Council (2 of 3)

#### **Adopt Resolution:**

- Authorizing the City Manager to Execute a Contract Amendment with Elite Landscape Construction, Inc in the Amount of \$26,090 for the Completion of Construction for the Earl Glenview Park; and
- Authorizing the City Manager to Execute a Contract Amendment with MIG, Inc. for in the Amount of \$6,400 for Final Design Services for the Earl Glenview Park; and
- Accepting the Earl Glenview Park as Complete and Authorizing the Filing of Notice of Completion with the San Mateo County Recorder's Office

# Request to City Council (3 of 3)

Adopt Resolution Authorizing the City Manager to Release \$250,000 of Project Retention to Graniterock Construction for the Crestmoor Neighborhood Reconstruction — Phase IV Street Improvement Project.

# **Questions and Feedback**

# **History**

- September 9, 2010 PG&E gas pipeline explosion and fire
- Fall/Spring 2011 Immediate cleanup and reconstruction
- March 2011 Trust Fund (\$50 Million)
   established for City's use for immediate and long
   term impacts of explosion and fire
- <u>December 2011</u> City Council confirmed extent and scope of neighborhood reconstruction
- March 2012 City and PG&E agree to \$70
   Million settlement (for establishment of San Bruno Community Foundation)
